



University Construction Oversight Meeting

January 13, 2022



**Florida Agricultural and Mechanical University
Board of Trustees**



**University Construction Oversight Meeting
Thursday, January 13, 2022**

1:30 PM

Conference Call


AGENDA

- | | |
|---|---------------|
| I. Call to Order | Trustee Moore |
| II. Roll Call | Dr. Turner |
| III. Opening Remarks | Chair Lawson |
| IV. Major Capital Project Updates: Bragg Memorial Stadium | VP Brown |
| V. Questions | |
| VI. Adjournment | Trustee Moore |

Phase 2a - Bragg Memorial Stadium



Project Status Report:		Budget: \$8,000,000		Date: 1/13/2022	
Project #:	Project Name:	University Project Manager:	Project Status:		
BRFM 346	Bragg Stadium Renovation	Bodie Young / David Rosenfeld			
Design Status (% Complete):	Designer:	Substantial Completion Date:			
100%	Clemons Rutherford & Associates	August 31, 2022			
Construction Status (% Complete):	Contractor:	Occupancy Date:			
20%	Allstate Construction, Inc.	September 9, 2022			
<p>Design</p>					
<p>Timely Completion Risk: Severe weather, material delays, COVID Mitigation Strategy: Identifying critical path materials that could impact the schedule</p>					
Project Contracts:	Expenses:	Encumbrances:	Remaining:		
65%	0.26%	65%	35%		

FAMU Bragg Stadium Phase 2a – Action Item from Dec 1, 2021 BFF Committee Mtg

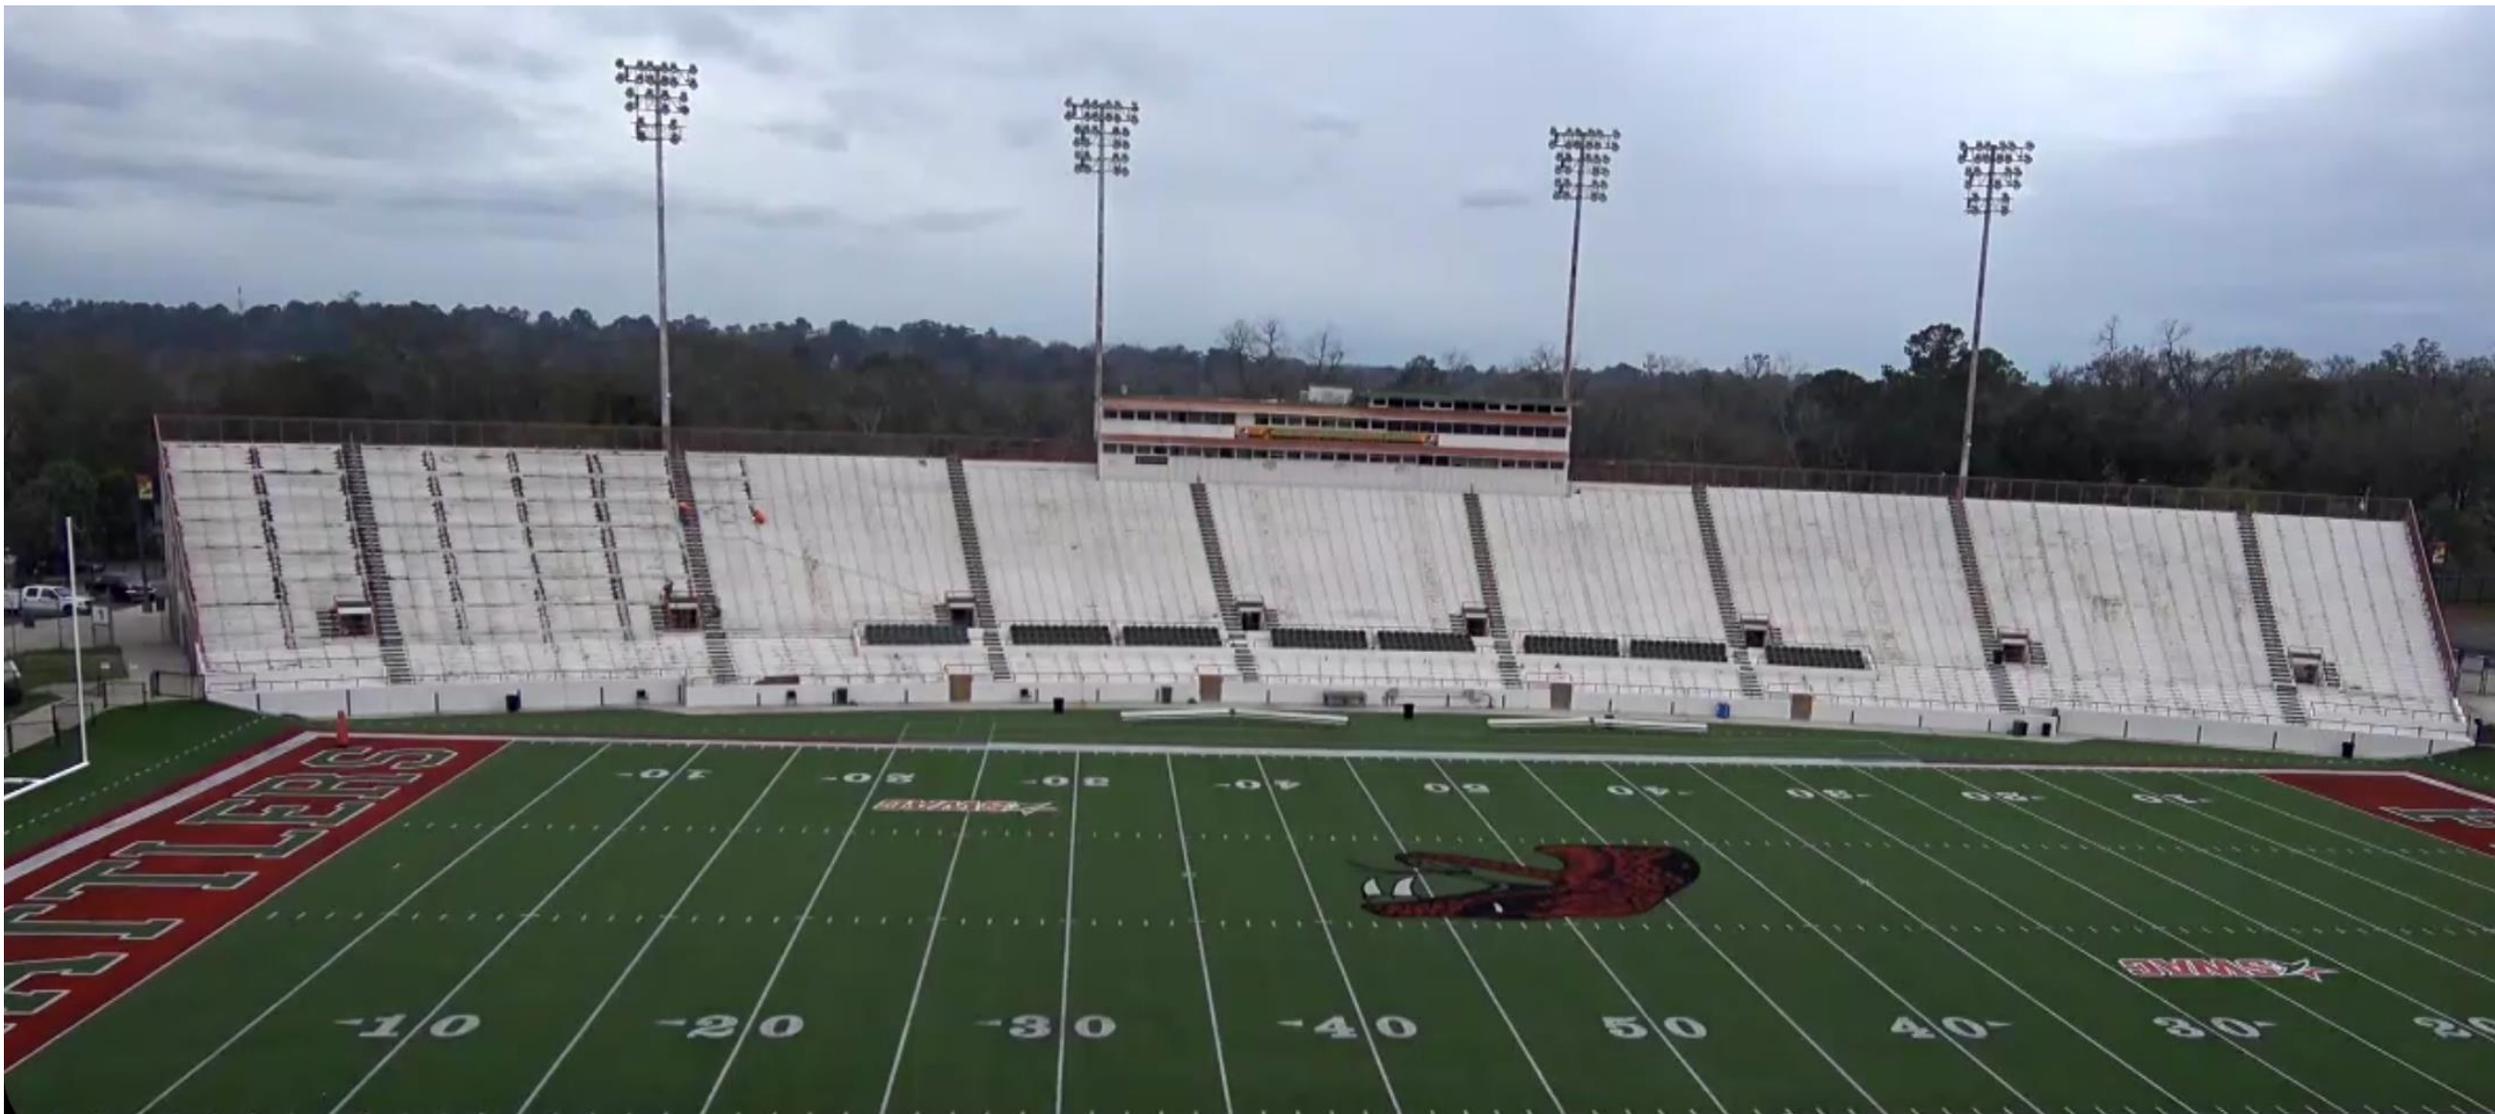

- Existing westside grandstands first two sections of the stadium steel pans has be cut from structural support to be removed by Crane.

FAMU Bragg Stadium Phase 2a – Construction Activities

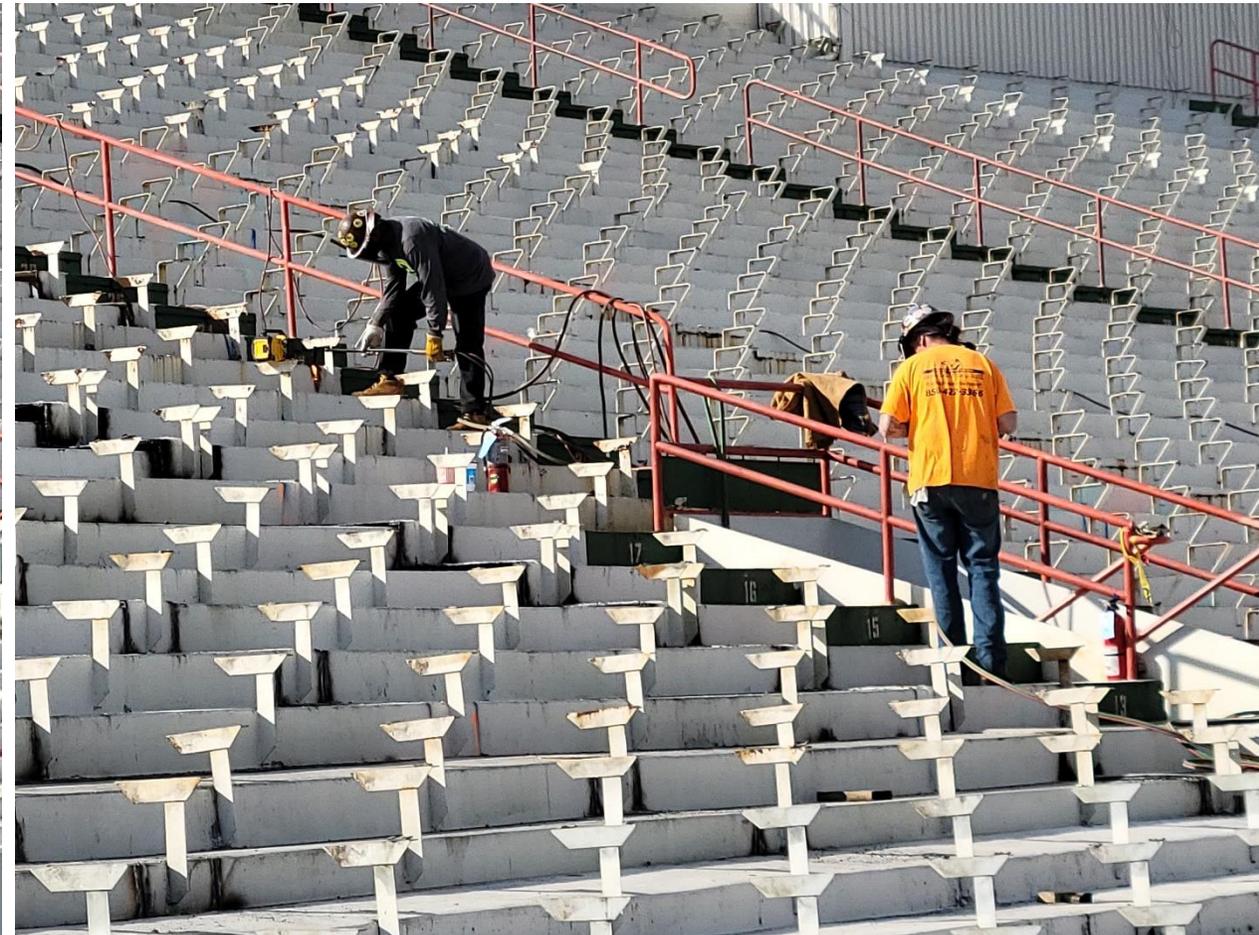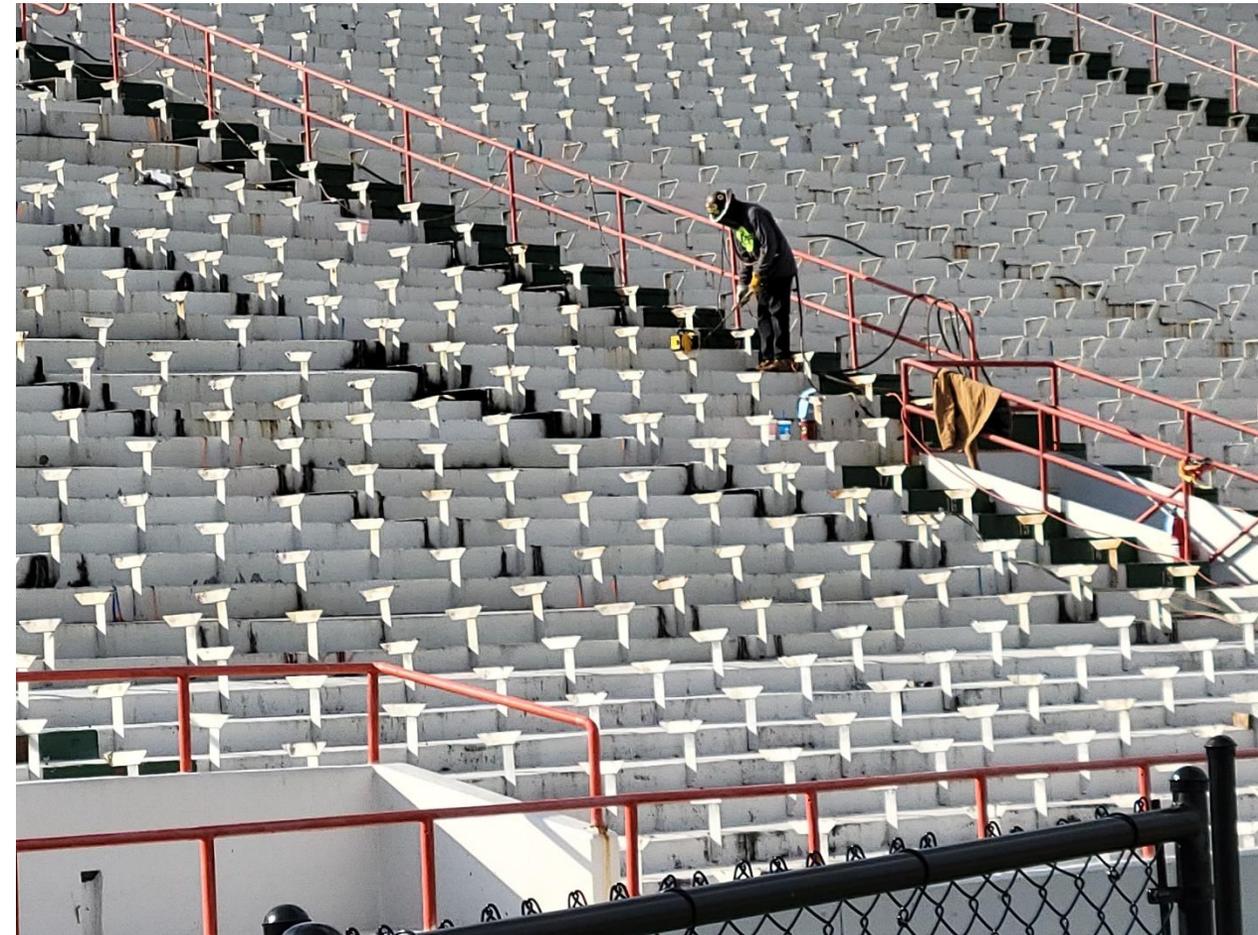

- Subcontractors cutting existing steel pans to be removed by Crane.

Questions

