

University Construction Oversight Meeting

Thursday, March 10, 2022



## Florida Agricultural and Mechanical University Board of Trustees



# University Construction Oversight Meeting Thursday, March 10, 2022 1:30 PM Conference Call

#### **AGENDA**

I. Call to Order Trustee Moore

II. Roll Call Dr. Turner

III. Opening Remarks Chair Lawson

IV. Major Capital Project Updates: Bragg Memorial Stadium VP Brown


V. Questions

VI. Adjournment Trustee Moore


## Phase 2a - Bragg Memorial Stadium

Project Status Reports	Budget: \$8,000,000		Date: 3/10/2022	
Project #:	Project Name:	University Project Manager:		Project Status:
BRFM 346	Bragg Stadium Renovation	Bodie Young / David Rosenfeld		
Design Status (% Complete):	Designer:	Substantial Completion Date:		
100%	Clemons Rutherford & Associates	August 31, 2022		Design
Construction Status (% Complete):	Contractor:	Occupancy Date:		
25%	Allstate Construction, Inc.	September 9, 2022		
Timely Completion Risk: Severe weather, material delays, COVID  Mitigation Strategy: Identifying critical path materials that could impact the schedule				
Project Contracts:	Expenses:	E	incumbrances:	Remaining:
\$7,253,050	\$288,205		\$7,253,050	\$6,964,845


#### **FAMU Bragg Stadium Phase 2a - Project Schedule**

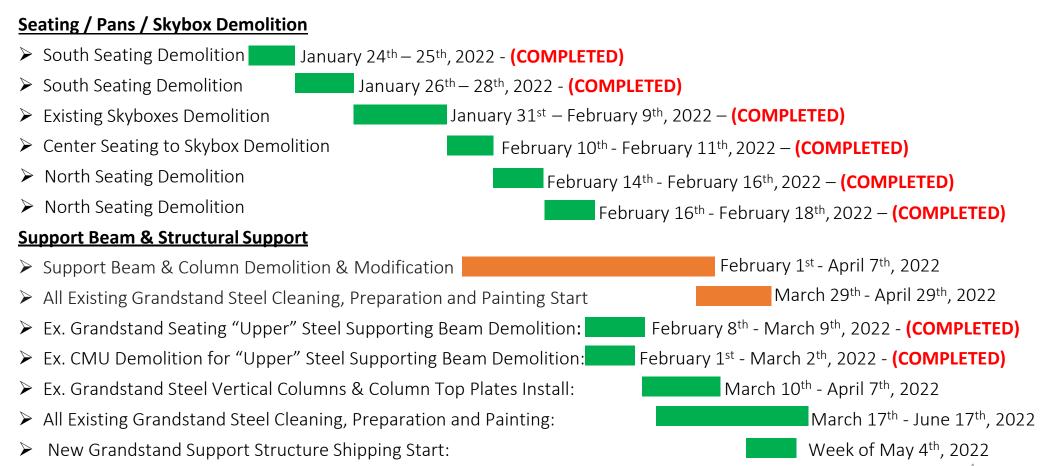


### **FAMU Bragg Stadium Phase 2a – Construction Activities**

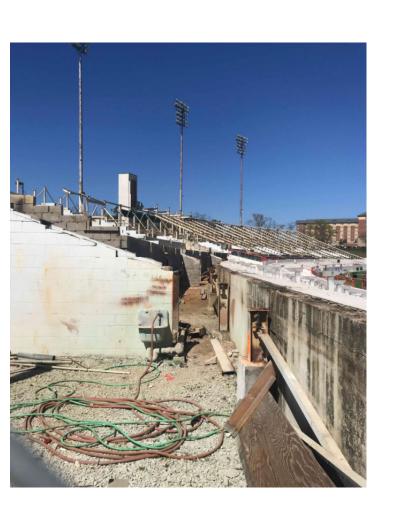



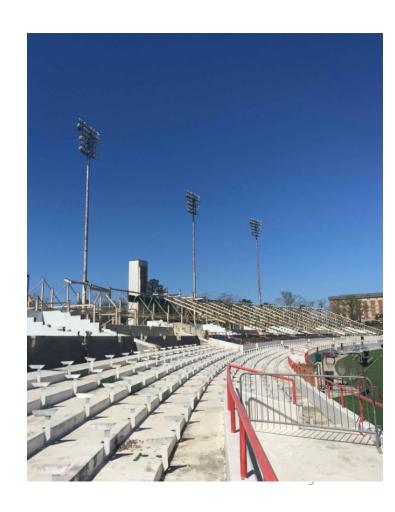

### FAMU Bragg Stadium Phase 2a – Construction Activities

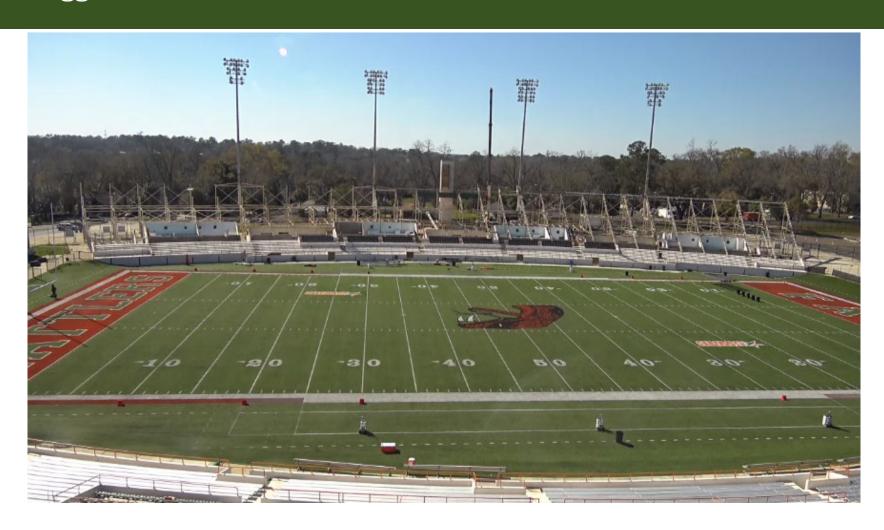



## Questions

